

MON/FAYETTE EXPRESSWAY

Construction Activity Weekly Updates



Planned Construction Activities for the Week of November 27, 2023

SECTION 53A1 • JEFFERSON HILLS BOROUGH, ALLEGHENY COUNTY


Contractor: Trumbull Corp

1. Work Shift

- The contractor is working 10-hour day shifts. The standard work shift is 7:00 AM to 5:00 PM, Monday to Thursday. Friday and Saturday shifts will be utilized as needed.

2. Traffic

- Coal Valley Road was closed October 9, 2023 near Walter's Road. A detour is delineated with signs. The closure is planned for approximately 6 months.
- The SR 885 truck crossing for large off-road trucks is being used. Flagging will be utilized when trucks are crossing the roadway and for stoppages during blasting.
- PTC 43 Southbound Ramp at Jefferson Boulevard has been shifted to the Northbound Ramp and crosses back over to Southbound side after bridge. Traffic from 51 Southbound on the flyover bridge has a stop condition at the end of the ramp. Please monitor speed thru this area.
- Brickyard Road will have traffic restrictions during working hours. No left turns are currently permitted from existing Brickyard Road onto SR 51.

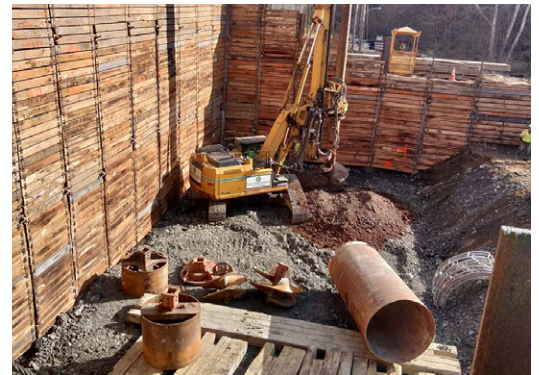

Pier foundation construction for the bridge over Camp Hollow Road.

3. Earthwork

- Sediment basins are constructed for runoff control. Runoff to be stored and slowly released.
- Blasting and excavation for the new highway that crosses under SR 885 continues.
- Blasting for mass excavation will continue through December 2025. For all blasts, 5 minutes prior to blasting the contractor will give 3 horn alerts of 15 seconds each. 1 minute prior to blasting, 3 horn alerts of 10 seconds will be sounded. 30 seconds prior to blasting, a series of short horn alerts will be sounded up to the time of detonation. After the blast, the area will be checked, and a horn will be sounded for 15 seconds to indicate that "all is clear". The warning sirens are intended to clear the work area and may or may not be heard at neighboring properties.

MON/FAYETTE EXPRESSWAY

Construction Activity Weekly Updates



Planned Construction Activities for the Week of November 27, 2023

4. Roadway and Bridge Work

- Bridge 400/401 over Brickyard Rd/SR 51/Peters Creek –The temporary shoring is installed at Abutment 1 and the contractor is installing micro-piles for the foundation. Piers and Abutment 2 have been completed.
- Bridge 402 over Jefferson Boulevard – Steel reinforcement bars are being installed for bridge deck.
- SR 885 Bridge 403 Abutment 1 and 2 concrete stems completed. Pier drilled shaft foundations are being constructed.

5. Noise/Dust/Runoff Control

- Erosion control measures are installed and will be modified as construction advances. The erosion controls will be maintained as necessary.
- Diversion ditches have been constructed to take runoff water to sediment basins.
- A street sweeper is on-site and will be used clean local roadways when needed.
- Water trucks are on-site and will be utilized to control dust when needed.

SECTION 53A1 – ESTIMATED COMPLETION DATE: Late 2026

Learn more about the Mon/Fayette Expressway by visiting the project website.
