

MON/FAYETTE EXPRESSWAY

Construction Activity Weekly Updates



Planned Construction Activities for the Week of September 29, 2025

SECTION 53A1 • JEFFERSON HILLS BOROUGH, ALLEGHENY COUNTY

Contractor: Trumbull Corporation

1. Work Shift

- The standard work shift is 6:00 AM to 4:30 PM, Monday to Thursday. Friday and Saturday shifts will be used as needed.

2. Traffic


- Coal Valley Road** – Coal Valley Road is scheduled to be closed again October 6, 2025 for a 3-4 weeks duration for slope restoration work. This is the last scheduled Coal Valley Road Closure.
- SR 885 Clairton Road** - There will be construction traffic and truck deliveries in this area.
- PTC 43/Jefferson Boulevard** - PTC 43 southbound drivers will be using the southbound ramp. Northbound drivers will cross over to the southbound side to Jefferson Boulevard. Please monitor speed and stay in your lane through the construction area.
- Jefferson Boulevard/SR 51** - Follow traffic signs, arrows, merging areas, stop and yield signs.
- Brickyard Road** – Completed.
- Pitt McKeesport Boulevard** – Utility relocation work is on going in this area for future projects.

3. Roadway and Bridge Work

- Bridge 400/401 over Brickyard Rd/SR 51/Peters Creek** - Majority of work on both bridges is completed.
- Bridge 402 over Jefferson Boulevard** - Majority of work is completed. Using as construction access across Jefferson Boulevard.



Brickyard Road asphalt paving.

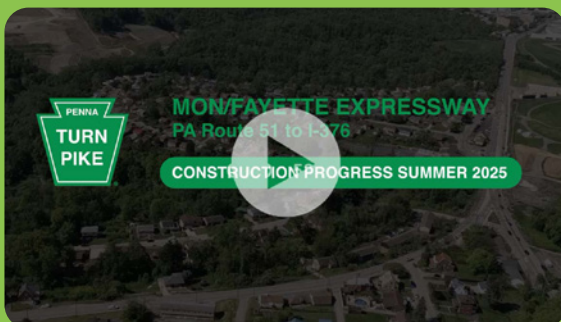

Throughout these weekly updates, you have seen construction progress along the Pennsylvania Turnpike Commission's Mon/Fayette Expressway in Allegheny County. We would now like you to come along for an exclusive ride as we show you an aerial progress report of the first two construction sections being built in West Mifflin and Jefferson Boroughs.

[WATCH THE VIDEO](#)

MON/FAYETTE EXPRESSWAY

Construction Activity Weekly Updates



Planned Construction Activities for the Week of September 29, 2025

- **Bridge 403 - SR 885 over 43** - Majority of work is completed. Open to traffic with construction traffic under bridge.
- **Bridge 404/405 over Coal Valley** - Northbound and southbound bridge barrier rebar installation. Barrier to be placed by slipform before winter.
- **Long Life Concrete Paving** continues on mainline and ramps from south end to north. Mainline 26' wide pavement has been completed. Filling in openings at shoulders and gore areas.
- **Toll Facility** - Toll facility building is being constructed. Interior finish work, electric installation.
- **Jefferson Boulevard** - Traffic is in a temporary configuration until the PTC 43 northbound off ramp is reopened. The Payne Hill Road entrance is open.



Stormwater management pond construction.

4. Noise/Dust/Runoff Control

- Erosion control measures are installed and will be modified as construction advances. The erosion controls will be maintained as necessary.
- Diversion ditches take runoff water to sediment basins.
- Sediment basins hold water for settlement and slow dispersion. Several sediment ponds are being converted to storm water basins.
- A street sweeper is on-site and will be used clean local roadways when needed.
- Water trucks are on-site and will be utilized to control dust when needed.

5. Trespassing on Construction Site

- The construction being performed in this area is a Limited Access Right-of-Way owned by the Pennsylvania Turnpike Commission. The construction areas are posted with No Trespassing/Private Property signs. **No pedestrians, ATVs or motorcycles should be entering the area.**
- Violators may be prosecuted under Section 3503(b)(1)(ii) which forbids criminal trespass.

SECTION 53A1 – ESTIMATED COMPLETION DATE: Late 2026

Learn more about the Mon/Fayette Expressway by visiting the project website.
